



City of Patterson
 Department of Engineering
 1 Plaza
 P.O. Box 667
 Patterson, CA 95363
 Phone (209) 895-8060 Fax (209) 895-8069

Measure L

City Name: City of Patterson

Project Name: Kinshire Street Improvements Project 2018-C-006

Date: 7/30/2021

Revenue		Expenses	
City Funds-Gas Tax		Project Budget	2,835,794
Federal Funds		Encumbered	
State Funds		Expended Measure L	118,807
Measure L Funds	2,535,794	Expended Other	
Other Funds-SB1	300,000	Available	2,716,986
Total	2,835,794		

Revenue and Expense include all aspects of the project that use Measure L Funds. Design, Construction and construction management are all included. Construction and Construction Management costs for phase 1 included at this time only. Design for both Phase 1 and Phase 2 are included. Expenses are current as of 7/30/21 for all project life, design costs only to date.

Construction is underway on Phase I but no construction invoices have been processed to date.

Completion Date: Estimated Completion Date for Phase 1 Construction November 30, 2021

Phase: Construction - phase I

Overall Project Details:

The project consists of a full depth reconstruct of the pavement section within the project area. The project is bounded by Sperry Avenue to the North, Poppy to the South, Clover to the West and Del Puerto Avenue to the East. The new pavement section was determined during the design process. In addition, all crosswalks and ramps within the project area will be removed and replaced, and constructed to meet the most current American with Disabilities Act (ADA) standards. Phase 1 design was completed in June of 2020. Phase 2 design is at 60% completion. The project went out to bid in June of 2020. Unfortunately, bids were higher than the Engineer's estimate. Subsequently, all bids were rejected. This project went out for rebid on February 24, 2021 and the contract was awarded on March 18, 2021. Construction is estimated to start May 2021 and the project is estimated to be completed by November 30, 2021. Phase I is currently in construction.


Project Status:

Proposal Due: February 19, 2019
Consultant Selection: May 8, 2019
City Council Approval: May 21, 2019
Design Contract Executed: June 20, 2019
Design Complete: March 6, 2020
Re-Advertise by: February 4, 2011

Construction Phase

Re-Bids Due: February 24, 2021
Contractor Selection: February 26, 2021
City Council Approval: March 16, 2021
Contract Executed: April 2, 2021
Construction Start: May 1, 2021
Estimated Project Completion: November 30, 2021

Add photos/renderings:

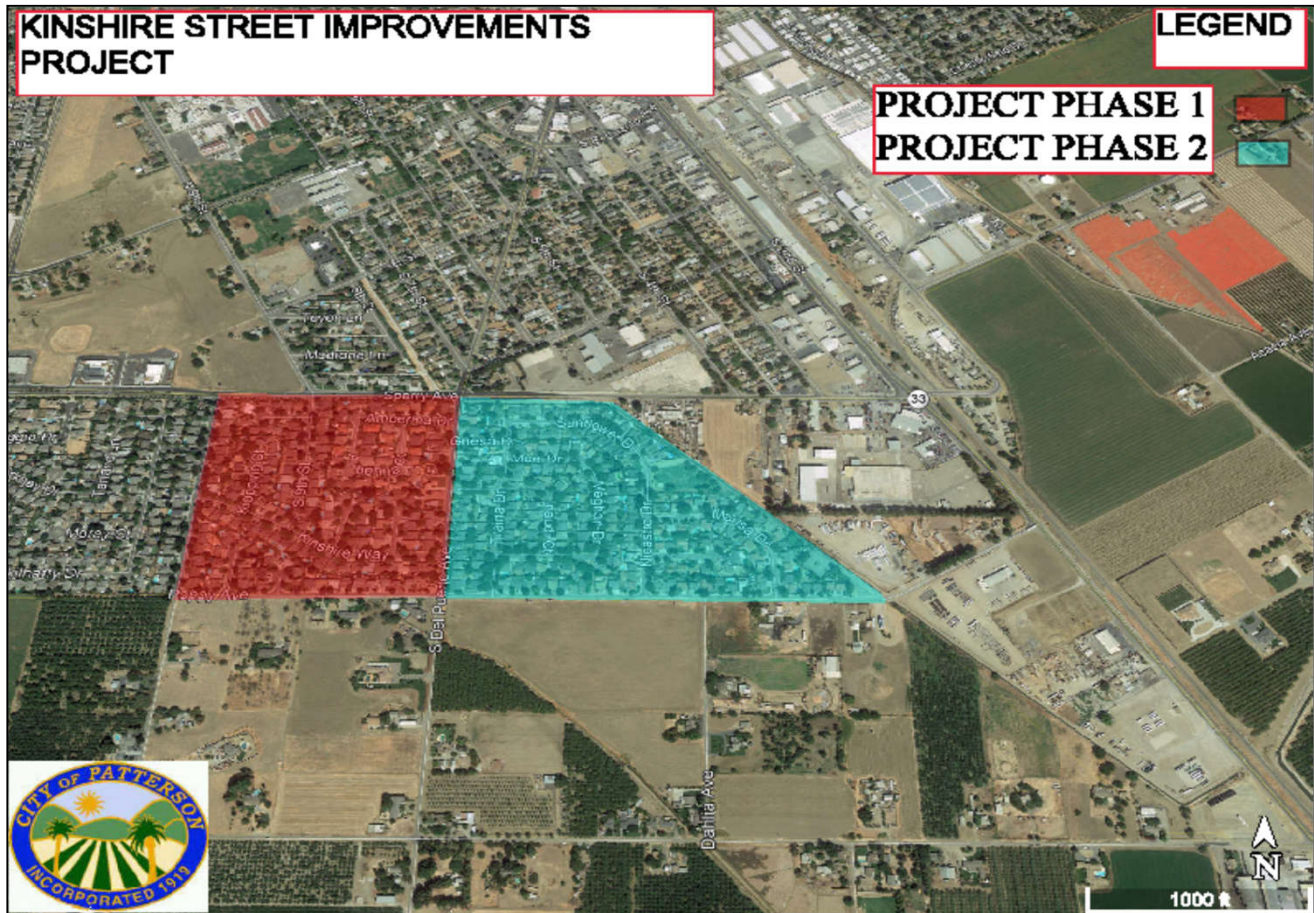



Measure L funding sign in place at Sperry Avenue and 9th Street
