



City of Patterson
Department of Engineering
1 Plaza
P.O. Box 667
Patterson, CA 95363
Phone (209) 895-8060 Fax (209) 895-8069

City Name: City of Patterson

Project Name: Las Palmas Avenue Overlay 2018-C-007

Date: 10/29/2021

| Revenue | | Expenses | |
|-------------------------------|------------------|---------------------|-----------|
| City Funds | 100,000 | Project Budget | 1,629,302 |
| Federal Funds-STBGP | 286,998 | Encumbered | |
| State Funds | | Expended: Measure L | 541,106 |
| Measure L Funds | 611,794 | Expended: Other | 824,641 |
| Other Funds-Cal Recycle Grant | 163,944 | | |
| Other Funds-SB1 | 466,567 | Available | 263,555 |
| Total | 1,629,302 | | |

Revenue and Expense include all aspects of the project that use Measure L Funds. Design, construction management and Construction all included. Expenses shown include all to date as of 10/22/21

Estimated Completion Date: 12/31/2021

Phase: Construction

Overall Project Details:

This project consists of a pavement overlay incorporating recycled asphalt. The project site is located along Las Palmas Avenue from Ward Avenue to the east end of the City limit in the Patterson, California. The road segment where construction will occur spans approximately 1.25 mile. Prior to overlaying, pavement surface with severe conditions will be excavated and reconstructed with aggregate base and asphalt concrete. The existing road will be cold planed where tying into the existing road sections and along existing gutter sections. All existing striping, markings, and markers shall be removed in preparation of an overlay, disposed of in accordance with regulations, and replaced with thermoplastic striping, markings, and reflective markers after the completion of an overlay. All existing manhole and valve covers are required to be raised to the final grade. In addition, all crosswalks within the project area shall be reconstructed to meet the most current Americans with Disabilities Act (ADA) Standards. This is an effort to maintaining and improving roadway safety within the City of Patterson.

The design phase of this project has been completed. The project went out to bid on Thursday, December 17, 2020, and the contract was awarded by City Council on February 2, 2021. Construction started March of 2021 and is estimated to be completed by September 2021. Construction is essentially complete. The final job walk is outstanding. Project should be accepted as complete by December 31, 2021.

Project Status:


Design Phase

Proposal Due: February 19, 2019
Consultant Selection: May 8, 2019
City Council Approval: May 21, 2019
Design Contract Executed: July 7, 2019
Design Complete: June 2020

Construction Phase

Bids Due: December 17, 2020
Contractor Selection: December 21, 2020
City Council Approval: February 2, 2021
Contract Executed: February 11, 2021
Estimated Project Completion: September 30, 2021

Add photos/renderings:

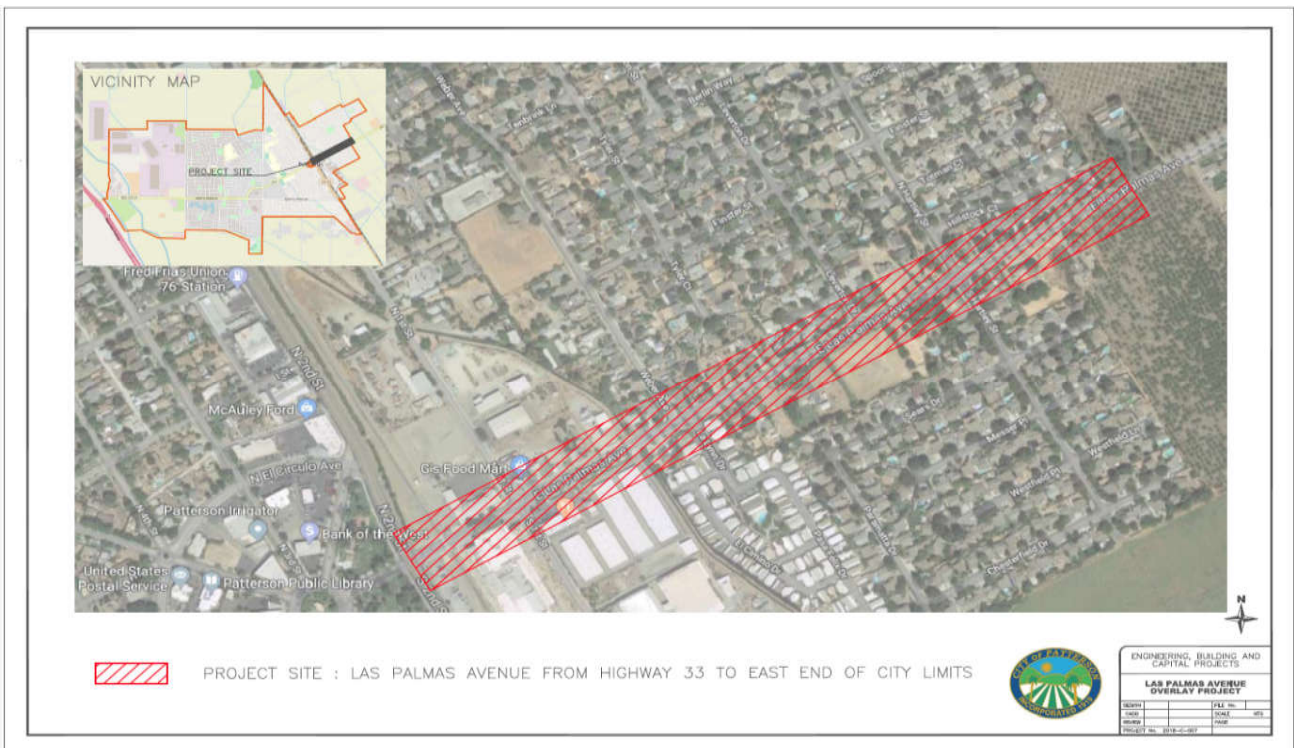



Measure L Funding Sign in Place



Paving at Las Palmas Avenue and First Street
